


# WRAC Update

## 8 June 2006



# the Restoration

## of America's Everglades & the South Florida Ecosystem



# South Florida Ecosystem Restoration

## Current Program

Modified Water  
Deliveries to  
ENP

Kissimmee  
River  
Restoration

Critical  
Projects  
Program

Continuing  
Authorities  
Program  
(1135, 206)

Central &  
Southern  
Florida  
Project

Upper  
St Johns

Manatee


C-51 / STA-1E

C-111

CERP





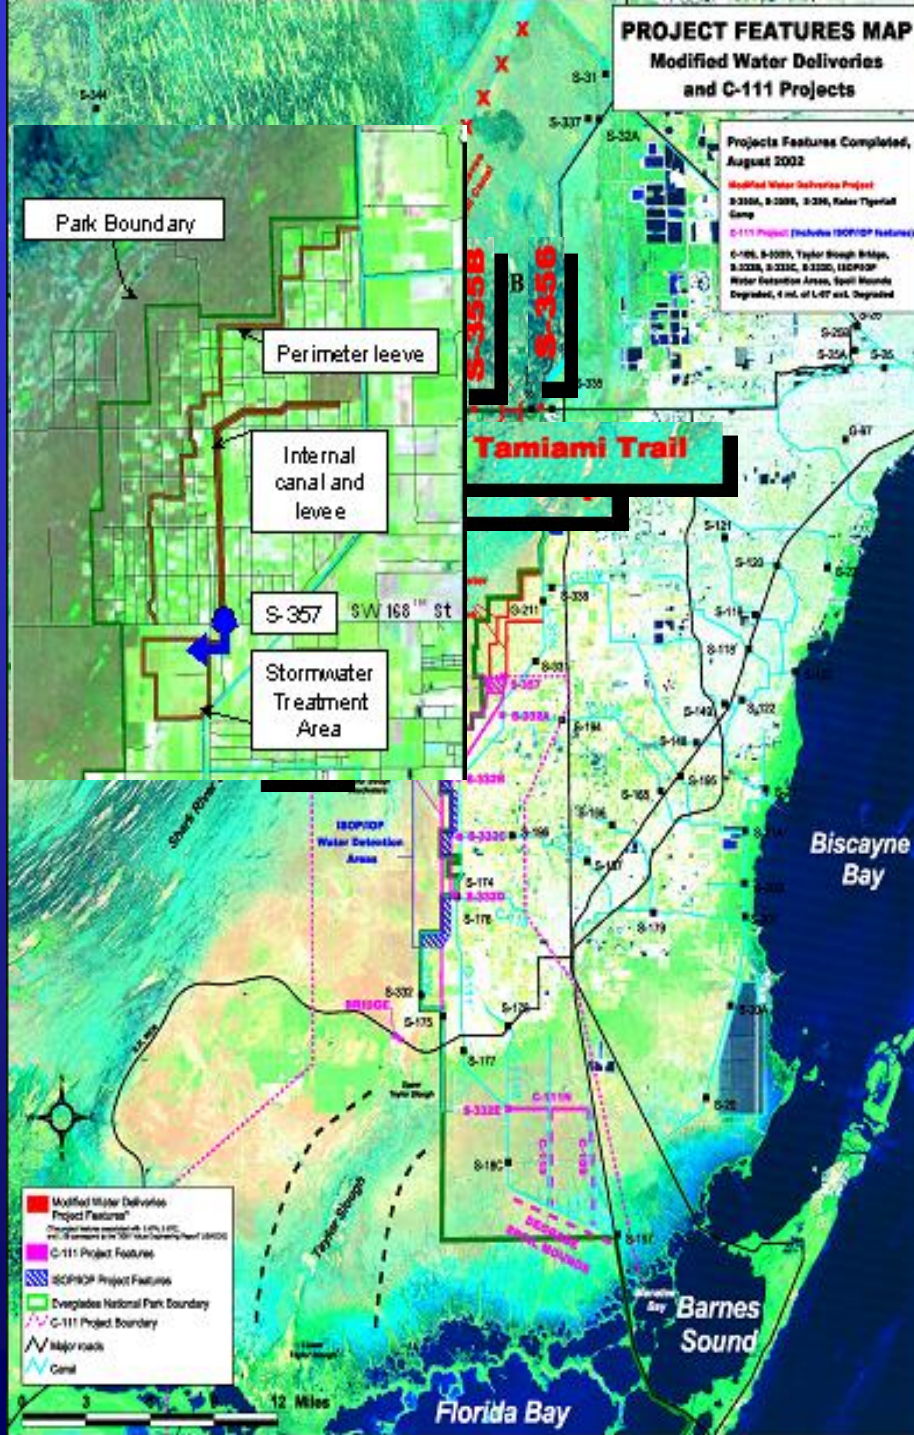

# MWD Project Completion Status

- Constructed S-355 A and S-355 B in L-29 levee
- Raised Tigertail Camp
- Degraded lower 4 miles of the L-67 extension canal and levee
- Constructed Interim S-356 pump station for seepage control
- Contact awarded for construction of Alternative 6D for the 8.5 SMA
- Final RGRR/SEIS for Tamiami Trail Modifications

# **8.5 SMA Contract Underway**

**Awarded on 20 Sept 2005**


**For \$16.99 million – 395 days**

- **Current completion - March 2007**
- **HTRW discoveries have delayed contractor and resulted in cost increased to handle items**
- **Demolition of existing structures and construction continuing**
- **Continuing to work FPL issues as construction progresses.**
- **Illegal dumping continues as a problem**

# Tamiami Trail - Selected Plan

## 2 Mile Bridge West and 1 Mile Bridge East

### Construction to Begin in 2007

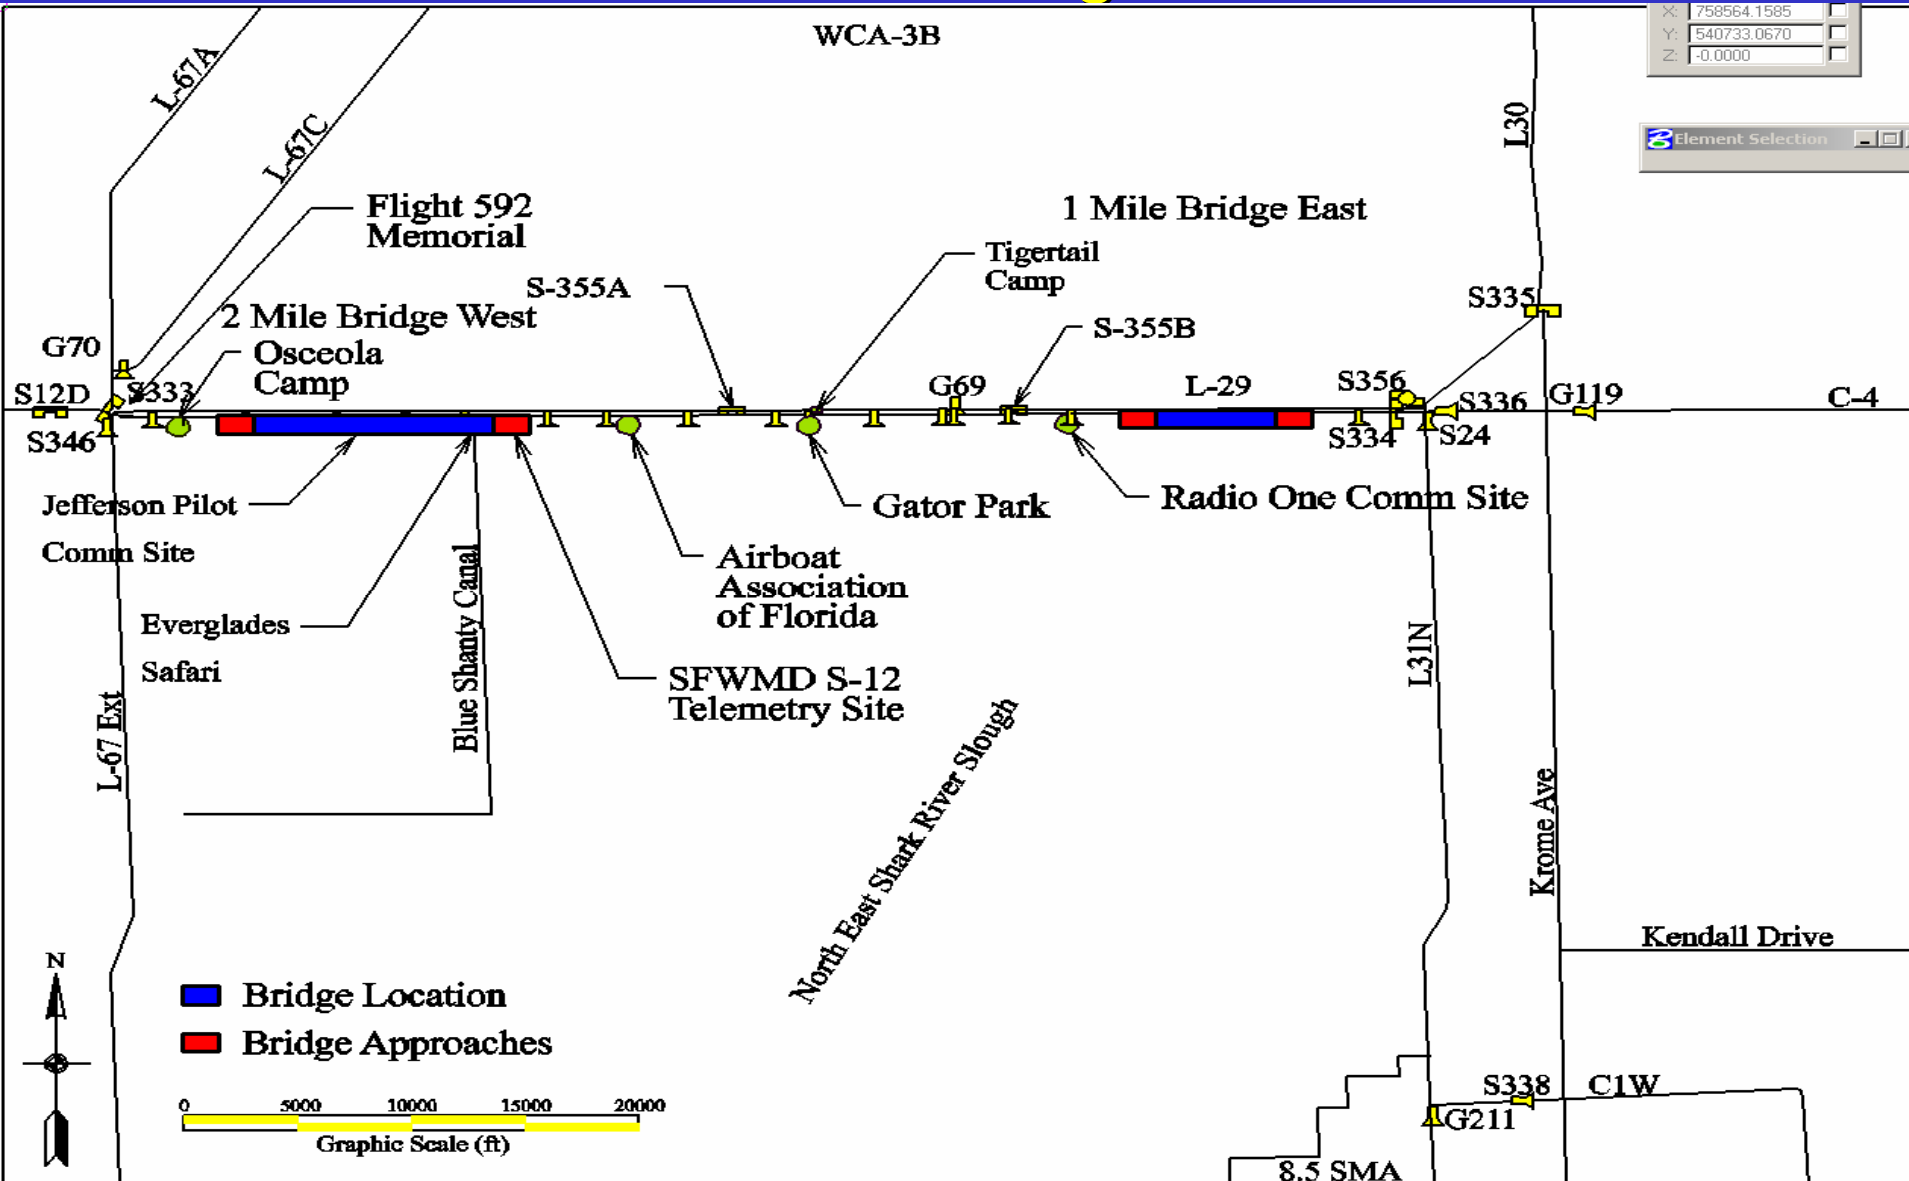

# Tamiami Trail

- 30% Design ongoing - complete in July
- Design – Build Contract to be advertised in October 06
- Contract to be awarded in by end of 2006.
- Construction to be done in 3 phases –
  - Phase 1 – eastern 3 miles with 1 mile bridge
  - Phase 2 – to begin in Oct 07 for western 4.2 miles including 2 mile bridge
  - Phase 3 to begin in Oct 08 for center portion.

# Tamiami Trail

- Real Estate requirements and impacts to existing airboat operations are on critical path.
- Supplemental EIS being prepared to address potential real estate action needed to cover both road and high water impacts

**Questions?**

