

## **Table of Contents**

# 1. Overview of Project:

	Purpose of Project	· · · · · · · · · · · · · · · · · · ·
	Accuracy	
	Bench Marks	
	Survey Equipment Used	
	Leveling Methods	
	Vertical Datum for the Project	
	Completion Date	
	Construction	
2.	<b>Details of Staff Gauges:</b>	
	Staff Gauge Detail Summary Chart	
	Project Location Maps	<del></del>
	2R T1	
	C11U75	
	G75_HW	
	G86S_HW	
	G204_HW	<del></del>
	G204_TW	
	G205_HW	
	G205_TW	
	G206_HW	
	G206_TW	
	S38_HW	
	S38 TW	
	S38A_HW	
	S38C_TW	
	S144_HW	
	S144_TW	
	S145_HW	
	S145_TW	
	G54_HW	
	G54_TW	
	G58_TW	
	G86N_HW	
	S9_HW	
	S9_TW	
	S9A_HW	

S9A_1W	
S9XS_HW	
S13AW_HW	
S13AW_TW_	
S124_HW	
S124_TW	
S125_HW	
S125_TW	
S381_HW	
S381_TW	
3A-NE	
3A-NE-GW	
G3A12	
L28S2	
L28S2 New Benchmark Sheet	
LHPS_HW	
LHPS_TW	
PGAWUZ GWT	
PGAW02_GW2	
WCA201	
WCA2U1_GW1	
WCA2U1_GW2	
S9X-N	
roject Results:	
Deliverables to South Florida Water Management	
Legend	
Survey Notes	

#### **OVERVIEW OF PROJECT**

### **Purpose of Project:**

Procure all materials to construct and install 43 staff gauges calibrated to the North American Vertical Datum of 1988 (NAVD88) at various sites identified by the Vertical Datum Project Manager. Establish a NAVD88 Reference Elevation on the inside deck of existing Telemetry Stations and stamp site specific data onto a brass tag, using a steel stamp die set. The brass tags were delivered to SFWMD and would be installed by SFWMD Field Personnel during site inspections.

#### Accuracy:

Staff gauges have been set (adjusted) to the nearest two hundredth (.02') of a foot, and reference elevations established to the nearest hundredth (.01') of a foot. Elevations have been transferred from provided bench mark using a digital level, steel tape, and redundant measurements.

#### **Bench Marks:**

A bench mark was provided by SFWMD at each location, unless otherwise noted, and used to establish the reference elevation and calibrate each staff gauge.

#### **Survey Equipment Used:**

Topcon DL-502 (Digital Level) Fiberglass Digital Level Rods Conventional Level Rod

#### **Vertical Datum Factor:**

The reference elevations and staff gauges, in this report, have been correctly calibrated to the North American Vertical Datum of 1988. The datum conversion to the National Geodetic Vertical Datum of 1929 (NGVD 29), as shown herein and engraved on each gauge, were provided by the SFWMD VDUP Project Manager.

#### **Completion Date:**

Staff Gauge installation, calibration, and the establishment of telemetry station reference elevation was completed on April 15, 2016.

#### **Construction:**

Each Staff Gauge is attached to a 4" O.D. galvanized steel pipe with stainless steel hardware. The pipes were driven to a depth to achieve required stability, to a minimum of 10', unless otherwise noted. Sections of pipes were driven by jack hammer, and attached with a galvanized threaded coupling.

# **Details of Staff Gauges**

## **Staff Gauge Detail Summary Chart:**

## Gauges completed:


					-	
Staff Gauge	Latitude	Longitude	Bench- mark	Benchmark Elevation	Well Head Reference	Conversion Elevation
Site	Editidde	Longitude	Used	NAVD88	BM	to NGVD29
					Elevation	
2B-T1	26° 07′ 46.309″	80° 21′ 58.179″	H695	8.42	13.00	1.54
C11U75	26° 03′ 47.437″	80° 21′ 48.717″	C11U75	7.748	10.56	1.56
G75_HW	27° 05′ 30.176″	81° 00′ 23.067″	FCE4544	25.84	27.79	1.28
G86S_HW	26° 03′ 34.236″	80° 26′ 05.026″	G86S	4.36	7.14	1.50
G204_HW	26° 19′ 57.113″	80° 45′ 53.221″	B50	13.11	20.11	1.44
G204_TW	26° 19′ 55.93″	80° 45′ 54.007″	B50	13.11	20.48	1.44
G205_HW	26° 19′ 59.074″	80° 43′ 00.333″	B53	12.53	20.50	1.45
G205_TW	26° 19′ 57.793″	80° 43′ 01.145″	B53	12.53	19.94	1.45
G206_HW	26° 20′ 00.85″	80° 39′ 08.923″	B57	12.28	18.48	1.45
G206_TW	26° 19′ 59.684″	80° 39′ 09.594″	B57	12.28	18.42	1.45
S38_HW	26° 13′ 46.184″	80° 17′ 55.974″	B43	17.506	18.62	1.54
S38_TW	26° 13′ 46.182″	80° 17′ 53.67″	B43	17.506	14.43	1.54
S38A_HW	26° 13′ 48.933″	80° 17′ 53.555″	B43	17.506	14.92	1.54
S38C_TW	26° 13′ 42.088″	80° 17′ 53.723″	B43	17.506	14.21	1.54
S144_HW	26° 13′ 06.392″	80° 23′ 51.664″	W464	15.92	17.79	1.50
S144_TW	26° 13′ 05.251″	80° 23′ 51.709″	W464	15.92	16.86	1.50
S145_HW	26° 13′ 19.253″	26° 13′ 19.253″	Y464	16.14	18.31	1.52
S145_TW	26° 13′ 18.06″	80° 21′ 56.696″	Y464	16.14	16.35	1.52
G54_HW	26° 05′ 41.898″	80° 13′ 49.898″	10.462	8.93	11.93	1.60
G54_TW	26° 05′ 41.099″	80° 13′ 45.249″	10.462	8.93	11.94	1.60
G58_TW	25° 53′ 58.786″	80° 09′ 43.676″	G58	7.456		1.56
G86N_HW	26° 03′ 42.555″	80° 26′ 04.957″	G86N	13.34	9.45	1.50
S9_HW	26° 03′ 41.894″	80° 26′ 35.755″	FCE1566	7.155	26.44	1.50
S9_TW	26° 03′ 41.755″	80° 26′ 37.527″	FCE1566	7.155	26.41	1.50
S9A_HW	26° 03′ 42.189″	80° 26′ 35.674″	FCE1566	7.155	11.25	1.50
S9A_TW	26° 03′ 42.706″	80° 26′ 38.475″	FCE1566	7.155	13.63	1.50
S9XS_HW	26° 03′ 36.36″	80° 26′ 35.65″	FCE1566	7.155	9.49	1.50
S13AW_HW	26° 03′ 52.611″	80° 16′ 55.03″	S.N.R 10	7.787	9.12	1.61
S13AW_TW	26° 03′ 52.678″	80° 16′ 51.652″	S.N.R 10	7.787	9.60	1.61
S124_HW	26° 07′ 46.155″	80° 21′ 56.05″	K697	6.99	8.68	1.54
S124_TW	26° 07′ 45.128″	80° 21′ 57.251″	K697	6.99	9.53	1.54
S125_HW	26° 09′ 51.679″	80° 17′ 52.443″	S125	6.457	10.32	1.56
S125_TW	26° 09′ 49.681″	80° 17′ 52.607″	S125	6.457	10.96	1.56
S381_HW	26° 03′ 41.305″	80° 25′ 12.524″	S381	6.049	9.44	1.51
S381_TW	26° 03′ 42.213″	80° 25′ 07.513″	S381	6.049	10.31	1.51

Staff Gauge Site	Latitude	Longitude	Bench- mark Used	Benchmark Elevation NAVD88	Well Head Reference BM Elevation	Conversion Elevation to NGVD29
3A-NE	26°16'8.00"	80°36'52.40"	3ANE	11.25	17.05	1.46
3A-NE_GW	26°16'8.00"	80°36'52.40"	3ANE	11.25	18.05	1.46
G3A12	26°10'14.20"	80°40'56.00"	3A12	11.72	16.89	1.46
L28S2	26° 05′ 37.32″	80° 50′ 06.223″	L28S2	12.838	17.13	1.46
LHPS_HW	26° 09′ 54.098″	80° 15′ 04.526″	LHPS	9.649	11.70	1.57
LHPS_TW	26° 09′ 51.768″	80° 15′ 05.187″	LHPS	9.649	13.40	1.57
PGAW02_GW1	26° 50′ 27.98″	80° 09′ 59.03″	Brockway Az Mk	23.134	17.96	1.52
PGAW02_GW2	26° 50′ 27.98″	80° 09′ 59.03″	Brockway Az Mk	23.134	17.95	1.52
WCA2U1	26° 14′ 27.31″	80° 21′ 20.38″	WCA2U1	12.303	15.40	1.52
WCA2U1_GW1	26° 14′ 27.31″	80° 21′ 20.38″	WCA2U1	12.303	15.22	1.52
WCA2U1_GW2	26° 14′ 27.31″	80° 21′ 20.38″	WCA2U1	12.303	15.22	1.52
S9X-N	26°03′43.8″	80°26′35.00″	FCE 1566	7.155		1.50

• All Elevations shown are NAVD 88

## **Project Location Maps:**

## **Overall Site**

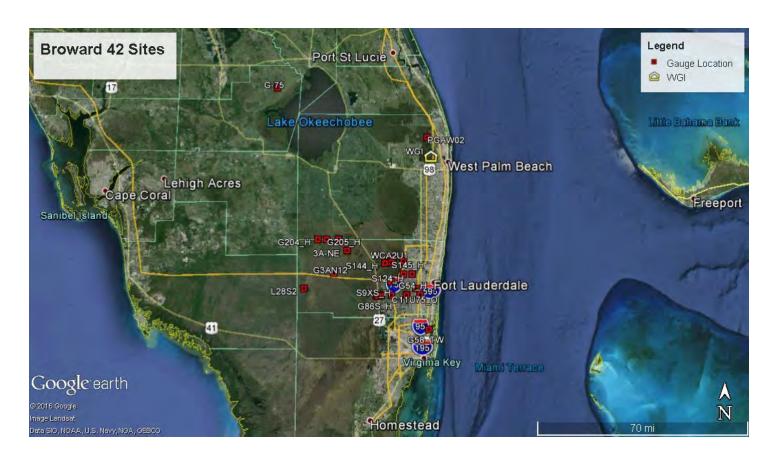

## Stage Recorder Site: PGAW02\_GW1

Party Chief:	Field Book Number:		Page Number:		
Ray Miller	613/	BK 11	47		
Benchmark Elevation	Date of Field Work:		Datum Offset to NGVD 29:		
(NAVD 88): 23.134	March 7	7, 2016	+1.52		
Benchmark Agency:	Benchmark Type:		Benchmark Stamp:		
SFWMD	Brass Disk		Brockway AZ Mk 1970/198		
Reference Elevation (N.	AVD88):	Existing Tag Elevation (Datum):			
			17.96 NAVD88		
Latitude:		Longitude:			
26° 50′ 27.98″		80° 09′ 59.03″			

Notes: Well elevation published in NAVD88 and checked in field. Tags not reset.

Removed Old Board: Existing gauge removed, mounting poles not removed.

Photographs:

Overall Site:




**Benchmark Location:** 



Benchmark Close Up:



Brass Tag Close Up:



Reference Mark:



Brass Tag & Reference:



New Staff Gauge:

Front View:



Side View:



## Stage Recorder Site: PGAW02\_GW2

Party Chief:	Field Book	Number:	Page Number:		
Jose Mendoza	613/	BK 11	47		
Benchmark Elevation	Date of Fi	eld Work:	Datum Offset to NGVD 29:		
(NAVD 88): 23.134	March <sup>-</sup>	7, 2016	+1.52		
Benchmark Agency:	Benchma	ark Type:	Benchmark Stamp:		
SFWMD	Brass	Disk	Brockway AZ Mk 1970/1987		
Reference Elevation (N.	AVD88):	Existing	Tag Elevation (Datum): 17.95 NAVD88		
Latitude:			Longitude:		
26° 50′ 27.98″		80° 09′ 59.03″			
Notes: Well elevation published in NAVD88 and checked in field. Tags not reset.					

## Photographs:

## Overall Site:

Removed Old Board:



## **Benchmark Location:**



Benchmark Close Up:



Brass Tag Close Up:



<u>Reference Mark:</u>



Brass Tag & Reference:



# **Project Results**

### **Deliverable Items to South Florida Water Management District:**

The following items were delivered to South Florida Water Management District with this Surveyor's Report. Neither the report nor the items listed below are complete without the other.

A CD Containing the following digital information:

- Survey Report in PDF Format
- Digital Photos of Set Staff Gauges
- Electronic Copy of Field Notes in PDF Format

#### Legend:

BM – Bench Mark

NAVD 88 – North American Vertical Datum of 1988

NGVD 29 – National Geodetic Vertical Datum of 1929

NGS – National Geodetic Survey

SFWMD – South Florida Water Management District

ACOE – Army Corp of Engineers

O.D. – Outside Diameter

#### **Survey Notes:**

- 1. Survey map & report, or copies thereof, are not valid without the signature and the original raised seal of a Florida Licensed Surveyor and Mapper.
- 2. Additions or deletions to the survey maps or reports by other than the signing party or parties are prohibited without the written consent of the signing party or parties.
- 3. The purpose of the survey is to show results of establishing reference elevations and calibrating staff gauges, as shown herein.
- 4. Latitude and longitude, as shown on page 5, was provided by the District and not verified as part of this survey.
- 5. Pursuant to client's request, the face boards of old NGVD 29 staff gauges were removed when possible. Posts were not removed.
- 6. New 4" galvanized posts were driven to a minimum depth of 10' below ground, unless otherwise noted in field notes. All pipes were structurally stable and plumb at time of installation.

## **Surveyor's Certification:**

I hereby certify that this Specific Purpose Survey meets applicable portions of the Minimum Technical Standards set forth by the Florida Board of Professional Surveyors and Mappers in Chapter 5J-17, Florida Administrative Code. This report is prepared for the sole and specific use of the South Florida Water Management District and is not assignable. All NAVD88 staff gauges were calibrated to a vertical accuracy of +/- 0.02' and reference elevations calibrated to a vertical accuracy of +/- 0.01'.

Wantman Group, Inc.

2035 Vista Parkway

West Palm Beach, FL 33411

L.B. Number 7055

By:

Derek G. Zeman, PSM
State of Florida
Certificate No. LS5655

3-7-16			SFU	Tim	1-		
MILLER				AWOZ			
PEREZ			10	70002			
1 CAE Z							157
BS RH	BS Dis		FS RH	F3 DIS	ELEV	Disc	
1.72	152.7				23.134		45 BRASS
			2 776	245.8			TOP BOH
2,425	464.L		2.119	0.0.0	J, 233	110	01 501
			5.00	63.0	179117	Mens	Cowi
4,782	62.0		5,000	0 0.0	11.197	MARKY	e Gwi
11 100	00.70		U 27/1	67.4	/7 000	100	02 %
			1, 179	07.4	11. 122	va) G-C	02 06
t.		++/	_	ECEV	Disc		
		- 1			APK (2)	Garage	weu
4.11		22.07	21	,,,-	Vian (9)	7001	W4.C
		. , .	4.19	1790	TOP OF S	30 (4A)	
3.81		21.69		17.01		or and	12
		101	3.73	17.96	VIND	Guan	WELL
			.,0		7 719	- GWZ	WELL
						57	
							E I
							7
			77.7				1
						-	
_							

